

43 Estabrook St, Phase 2  
Grafton, MA

### CURRENT PROJECT PHOTO (Photo taken on 04/15/16)

### SITE INFORMATION



The site is one parcel of land consisting approximately 55.32 acres of residential/agriculturally-zoned land. The majority of the site is comprised of undeveloped cleared land used as agricultural fields for hay production.

### SYSTEM INFORMATION

Utility:	NGRID	Load Zone:	WCMA
Type:	Ground Mount		
		Permit	Actual
System Size MWac:		2.700	2.700
System Size MWdc:		3.704	3.704

### DEVELOPMENT PROJECT TEAM

Project Executive:	Aidan Foley
Project Manager:	Mike Marsh
Analyst:	Kathryne Cleary

### PROJECT HEALTH

Health	Stage	Name	Description (brief)	Typ. Dur.	Act. Dur.	Comment
●	Stage 1	Acquisition	LOA, IX App, Site Analysis	3 months	4 months	
●	Stage 2	Development	Regulatory Permits, Impact study	6 months	5 months	
●	Stage 3	Pre-Construction	EPC RFP bid/award, Final Appvls	3 months	2.5 months	
●	Stage 4	Construction	Permission to Operate (PTO)	5 months	TBD	Forecasted 4-mnths
●	Stage 5	Stabilization	Sub. Completion, Utility PTP	20 years	TBD	-

KEY	● No issues, progressing without issues at this time.	● Some issues, but will likely be resolved. [Comments required]	● Significant issues that will adversely impact system size, schedule, etc. [Comments required]
-----	---	---	---

### BUDGET

The project remains tracking/forecasting to remain on budget, within nothing more to report at this time.

### SCHEDULE

Pro Tech has issued a revised schedule since the last project update was released. All values in the Key Milestone Dates table below have been updated. The project is now projected to reach completion earlier than previously anticipated.

### KEY MILESTONE DATES

02/01/16	Site Mobilization
04/06/16	Racking Completion
04/18/16	Modules Completion
05/20/16	Electrical Completion
05/20/16	Mechanical Completion
05/30/16	Witness Test Date
05/30/16	COD
06/01/16	Substantial Completion
07/21/16	Final Completion

### KEY EQUIPMENT PROCUREMENT & COMMISSIONING DATES

Item	Del. Date	Actual	Comments
DAS	05/30/16		
Racking	02/29/16	03/05/16	
SH Modules	03/21/16	03/14/16	100% Received
CS Modules	03/21/16	03/14/16	25% Received
SMA Inverters	05/19/16	03/31/16	
Switchgear	05/30/16	04/14/16	
Transformer	07/11/16		
Comment:			

### PROJECT NOTES

Racking is about 95% complete. The installation of modules is approaching 50% completion, and the first 10 inverters have been hanged. Both DC and AC trenching are nearly 100% complete and work on the two equipment pads is underway. 100% of modules and 100% of inverters have been delivered on site, as have the project's two switchgears. The storm water management features on the site are also nearing completion.

**RECEIVED**

### ACTION ITEMS

None to report at this time.

**APR 26 2016**

### CURRENT PROJECT PHOTOS (taken 04/01/16 - 04/15/16)




April 5, 2016



April 5, 2016



April 5, 2016

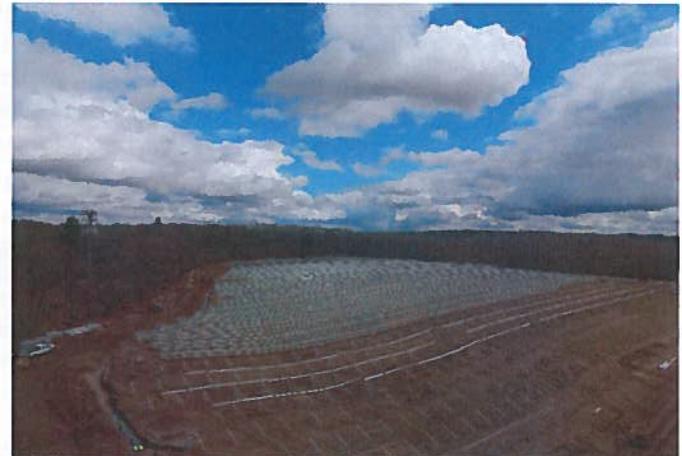

April 8, 2016



April 8, 2016



April 8, 2016

### CURRENT PROJECT PHOTOS (taken 04/01/16 - 04/15/16)



April 13, 2016



April 13, 2016



April 13, 2016



April 13, 2016



April 13, 2016



April 13, 2016

